FORM DR-0404-A
REV. 5-15-98
www.uprr.com

ENCASED FLAMMABLE PIPELINE CROSSING

NOTE: ALL AVAILABLE DIMENSIONS MUST BE FILLED IN TO PROCESS THIS APPLICATION.

PLACE ARROW INDICATING NORTH DIRECTION RELATIVE TO CROSSING

NO SCALE

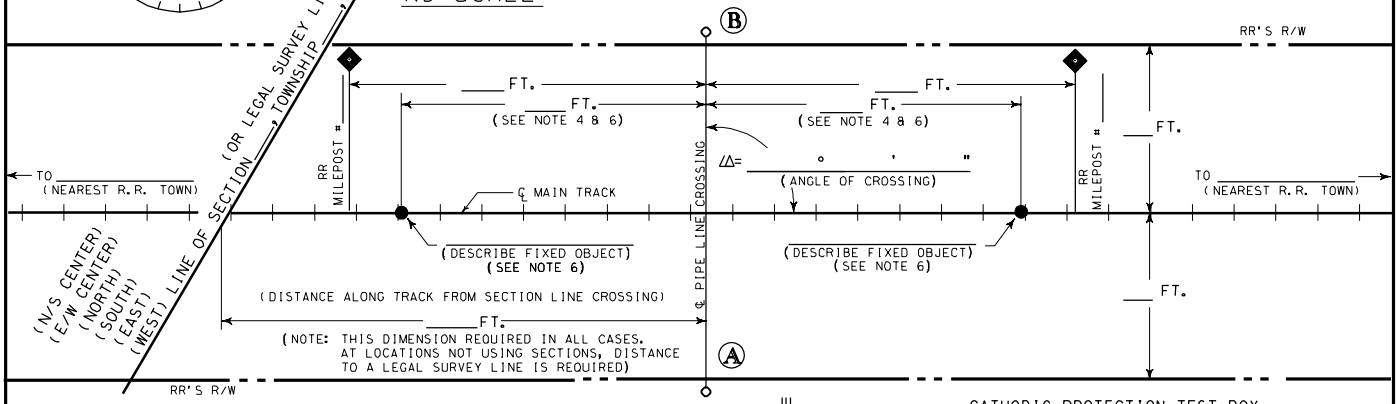

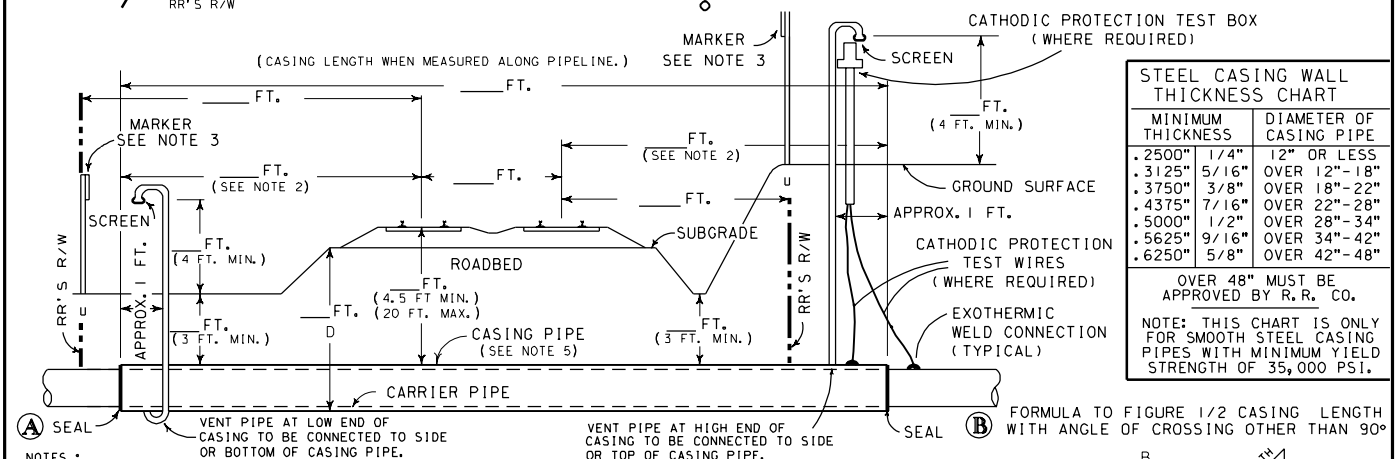

STEEL CASING WALL THICKNESS CHART

MINIMUM THICKNESS		DIAMETER OF CASING PIPE
.2500"	1/4"	12" OR LESS
.3125"	5/16"	OVER 12"-18"
.3750"	3/8"	OVER 18"-22"
.4375"	7/16"	OVER 22"-28"
.5000"	1/2"	OVER 28"-34"
.5625"	9/16"	OVER 34"-42"
.6250"	5/8"	OVER 42"-48"

OVER 48" MUST BE APPROVED BY R.R. CO.

NOTE: THIS CHART IS ONLY FOR SMOOTH STEEL CASING PIPES WITH MINIMUM YIELD STRENGTH OF 35,000 PSI.

FORMULA TO FIGURE 1/2 CASING LENGTH WITH ANGLE OF CROSSING OTHER THAN 90°



NOTES:
1) ALL HORIZONTAL DISTANCES TO BE MEASURED AT RIGHT ANGLES FROM ℄ OF TRACK.
2) CASING TO EXTEND BEYOND THE ℄ OF TRACK AT RIGHT ANGLES THE GREATER OF 2D + 20 FT., OR 45 FT., AND BEYOND LIMIT OF RAILROAD RIGHT-OF-WAY IF NECESSARY TO PROVIDE PROPER LENGTH OUTSIDE OF TRACK.
3) MARKER TO INDICATE LOCATION OF PIPELINE AT RIGHT-OF-WAY LINE. IN ADDITION, MARKERS SHALL BE INSTALLED AT MINIMUM 500 FT. INTERVALS ALONG PIPELINE ENCROACHMENTS AND AT LOCATIONS OF MAJOR CHANGE OF DIRECTION.
4) MINIMUM OF 50' FROM THE END OF ANY RAILROAD BRIDGE, ℄ OF ANY CULVERT, OR FROM ANY SWITCHING AREA.
5) SIGNAL REPRESENTATIVE MUST BE PRESENT DURING INSTALLATION IF RAILROAD SIGNALS ARE IN THE VICINITY OF CROSSING.
6) ALLOWABLE FIXED OBJECTS INCLUDE: BACKWALLS OF BRIDGES; ℄ OF ROAD CROSSINGS & OVERHEAD VIADUCTS (GIVE ROAD NAME), OR CULVERTS.
7) CASING AND CARRIER PIPE MUST BE PLACED A MINIMUM OF 2 FEET BELOW THE EXISTING FIBER OPTIC CABLE. ANY EXCAVATION REQUIRED WITHIN 5 FEET OF THE EXISTING FIBER OPTIC CABLE MUST BE HAND DUG.

A) IS PIPELINE CROSSING WITHIN DEDICATED STREET ?_____YES;_____NO;
B) IF YES, NAME OF STREET _____
D) DISTRIBUTION LINE _____ OR TRANSMISSION LINE _____
C) CARRIER PIPE :
COMMODITY TO BE CONVEYED_____
OPERATING PRESSURE_____PSI
WALL THICKNESS _____;DIAMETER_____;MATERIAL _____;
E) CASING PIPE :
WALL THICKNESS_____;DIAMETER_____;MATERIAL _____;
NOTE : CASING MUST HAVE 2" CLEARANCE BETWEEN GREATEST OUTSIDE DIAMETER OF CARRIER PIPE AND INTERIOR DIAMETER OF CASING PIPE. WHEN FURNISHING DIMENSIONS, GIVE OUTSIDE OF CARRIER PIPE AND INSIDE OF CASING PIPE.
F) METHOD OF INSTALLING CASING PIPE UNDER TRACK(S):
_____DRY BORE AND JACK (WET BORE NOT PERMITTED) ;
_____TUNNEL ; OTHER_____
G) WILL CONSTRUCTION BE BY AN OUTSIDE CONTRACTOR?_____YES;_____NO;
H) DISTANCE FROM CENTER LINE OF TRACK TO NEAR FACE OF BORING AND JACKING PITS WHEN MEASURED AT RIGHT ANGLES TO TRACK_____ (30' MIN.)
I) APPLICANT HAS CONTACTED 1-800-336-9193, U. P. COMMUNICATION DEPARTMENT, AND HAS DETERMINED FIBER OPTIC CABLE_____DOES ;_____DOES NOT ; EXIST IN VICINITY OF WORK TO BE PERFORMED . TICKET NO. _____

EXHIBIT "A"

(FOR RAILROAD USE ONLY)

UNION PACIFIC RAILROAD CO.

_____
(SUBDIVISION)

M. P _____ E. S. _____

ENCASED _____ CROSSING AT

_____
(NEAREST CITY) (COUNTY) (STATE)

_____
(APPLICANT)

RR FILE NO. _____ DATE _____

WARNING

IN ALL OCCASIONS, U. P. COMMUNICATIONS DEPARTMENT MUST BE CONTACTED IN ADVANCE OF ANY WORK TO DETERMINE EXISTENCE AND LOCATION OF FIBER OPTIC CABLE.
PHONE : 1-800-336-9193
